


Dryer - Commissioning Report

Dryer - Type and Serial No.					Commissioned By and Date					
Type: TAC-100					Name: MD.MAHABUB					
Serial No: 23090503					Training Passport Number: N/A					
					Date (dd/mm/yyyy): 31.12.2023					
Options Fitted / Installed										
Receiver: N/A	Yes	V	No		Condensate Drain Valve:	Yes	V	No		
Receiver Size (Litres): 2000L					By-pass Installed:	Yes	Į.	No		
Receiver Drain Valve:	Yes	V	No		Local / Remote Control:	Yes		No	7	
Water Separator:	Yes	1	No		Flow Control Device:	Yes		No	V	
Pre-Filter:	Yes	V	No		Compressor Details					
Pre-Filter Type:	TAF-1	150T	-		Oil Free Compressor's:	Yes		No	7	
Pre-filter Sizes:	15 m3/min				Max Flow Rate: 6.8 m³/h					
After Filter:	Yes	V	No		Voltage: 389,382,388					
After Filter Type: TAF-150F					Amperage: 5.5, 5.5, 5.5					
Site Details				Sales Co. / Distributor Details						
Company: MARICO BANGLADESH LTD.					Sales Co. / Distributor: TRIDENT AGENCY LTD.					
Address: SHIRIRCHALA,BHABANIPUR,GAZIPUR SADAR ,GAZIPUR					Address: AWAL CENTER (9TH FLOOR), 34 KEMAL ATATURK AVENUE BANANI C/A, DHAKA, BANGLADESH.					
Postcode: 1700					Postcode: 1213.					
Contract: RIAD HOSSAIN				Contract: MOHAMMAD ALI						
Telephone:+8801716503481				Telephone: +8802 9821377-80.						
Email: hossain@marico.com				Email: info@tridentbd.com						
					Commissioning Engineer: MD. MAHABUE	BUR RA	AHAN	/AN		
					Commissioning Date: 31.12.2023					

Dryer Application											
FOR MANUFACTURING											
Site / Environmental Conditions					Installation Details						
Clean Site Conditions:		Yes	V	No		Cable Size: 4X4 rm n					
Installation Satisfactory:		Yes	V	No		Fuse Size:	REAKER 10 amps				
						Pipework Connect	tions as per guidelines:	Yes 🗹	No 🗆]	
If answered "No" (*), please give full d	etails in "Fu	urther C	Comme	ents" on	page 3.						
Operational Values											
Ambient Air Temperature:	32	°C	V	°F		Dewpoint Switch	ing:	Yes 🗹	No 🗆]	
Inlet Air Temperature:	36	°C	V	°F		Auto Fault Re-se	et:	Yes □	No 🗵]	
Inlet Pressure:	9.3	bar	7	psi		Auto Restart:		Yes \square	No 🗵]	
Outlet Pressure:	9.2	bar	7	psi		Alarm / Trip Dew	point: N/A	°C □	°F □]	
Dewpoint:	4.5	°C □ °F □				Alarm / Trip Pres	ssure: N/A	bar \square	psi 🗆]	
Purge Setting:	N/A	bar		psi		Alarm / Trip Tem	°C □	°F □]		
Hydrometer Installed:	N/A	Yes		No	7	Service Due:	Yes 🗆	No 🗵]		
		-									
Signatures		Prin	t				Sign	Date (dd/	mm/yyy	y)	
Operator:			МГ	ם וום	III AN	IN RIPON MD. RUHUL AMIN RIPON		31 12 2023			
Trainning Completed:	V		IVIL	KUH	IOL AI			31.12.2023			
Commissioning		MD. MAHA				ΛRI IR	MD. MAHABUB	31.12.2023			
Engineer:						ADOD	WID. WIAI IADOB				
Customer / End User:		DIADUAC			р пу	CCAN	RIAD HASSAN		24 42 2022		
		RIAD HAS				SSAIN	RIAD HASSAN	31.12.2023			
Further Comments:											

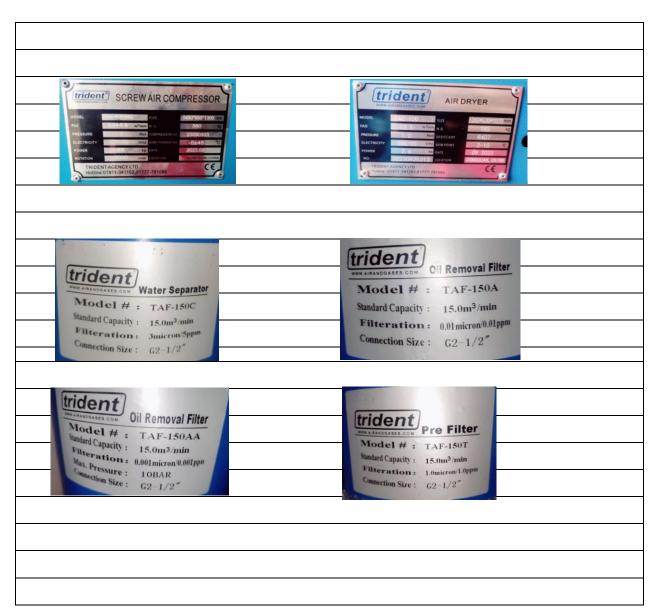

If possible, and where applicable, please supply photographic evidence of fault/failure
